










ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	t '06							09 Oct '06	
							T	W	T	F	S	S	M	T	
1	Strategic Plan (Phase One)	30 days	Wed 04/10/06	Tue 14/11/06											
2	MHSOP Development	30 days	Wed 04/10/06	Tue 14/11/06		Bob Feirn									
3	Parameters	30 days	Wed 04/10/06	Tue 14/11/06		Bob Feirn									
4	Medical Strategy	16 days	Mon 09/10/06	Mon 30/10/06											
5	Admissions criteria	16 days	Mon 09/10/06	Mon 30/10/06		N.A.W.									
6	Medical cover	16 days	Mon 09/10/06	Mon 30/10/06		N.A.W.									
7	Staff	30 days	Wed 04/10/06	Tue 14/11/06											
8	H.R. Processes - "at risk" etc	30 days	Wed 04/10/06	Tue 14/11/06		Bob Feirn; Mike Race;									
9	Impact assessment	0 days	Mon 09/10/06	Mon 09/10/06		Bob Feirn								◆ 09	
10	Race & equality	0 days	Mon 09/10/06	Mon 09/10/06										◆ 09	
11	Users	1 day	Mon 16/10/06	Mon 16/10/06											
12	Partner Information	1 day	Mon 16/10/06	Mon 16/10/06		Bob Feirn									
13	Carers information	1 day	Mon 16/10/06	Mon 16/10/06		Bob Feirn									
14	Close O.P outlying sites	16 days	Mon 23/10/06	Mon 13/11/06											
15	Transfer of County Wide Resources	16 days	Mon 23/10/06	Mon 13/11/06											
16	Vehicles	0 days	Wed 25/10/06	Wed 25/10/06		Bob Feirn									
17	Any other identifiable facilities	0 days	Wed 25/10/06	Wed 25/10/06		Team Managers									
18	Brownhill	6 days	Mon 23/10/06	Mon 30/10/06		Bob Feirn									
19	Removal	5 days	Mon 23/10/06	Fri 27/10/06		Richard Butt-Evans									
20	Decommissioning	1 day	Mon 30/10/06	Mon 30/10/06	19	Judith Morris									
21	Contracts	5 days	Mon 23/10/06	Fri 27/10/06		Steve Gully									
22	Stonebury	6 days	Mon 30/10/06	Mon 06/11/06		Bob Feirn									
23	Removal	5 days	Mon 30/10/06	Fri 03/11/06		Greta Barnett									
24	Decommissioning	1 day	Mon 06/11/06	Mon 06/11/06	23	Judith Morris									
25	Contracts	5 days	Mon 30/10/06	Fri 03/11/06		Lesley Cook									
26	Tyndale	6 days	Mon 06/11/06	Mon 13/11/06		Bob Feirn									
27	Removal	5 days	Mon 06/11/06	Fri 10/11/06		Maggie Porter									
28	Decommissioning	1 day	Mon 13/11/06	Mon 13/11/06	27	Judith Morris									
29	Contracts	5 days	Mon 06/11/06	Fri 10/11/06		Maggie Porter									
30	Open O.P CMHT Sites	7 days?	Mon 06/11/06	Tue 14/11/06		Bob Feirn									


Project: Community Changes 04.10.06
Date: Wed 11/10/06

Task		Milestone	◆	External Tasks	
Split		Summary		External Milestone	◆
Progress		Project Summary		Deadline	↓

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	t '06						09 Oct '06	
							T	W	T	F	S	S	M	T
31	Colliers Court	1 day?	Tue 07/11/06	Tue 07/11/06	22	Lesley Cook								
32	Room availability	1 day?	Tue 07/11/06	Tue 07/11/06		Paul Jolley;Lesley Coc								
33	Weavers Croft	1 day?	Tue 14/11/06	Tue 14/11/06	26	Bob Feirn								
34	Room availability	1 day?	Tue 14/11/06	Tue 14/11/06		Pat Burdett								
35	Holly House	1 day?	Mon 06/11/06	Mon 06/11/06		Bob Feirn								
36	Establish Community Team base office	1 day?	Mon 06/11/06	Mon 06/11/06										
37	Room availability	1 day?	Mon 06/11/06	Mon 06/11/06		Jan Furniaux;Marika F								
38	Charlton Lane Centre Day Treatment	1 day?	Mon 06/11/06	Mon 06/11/06		Bob Feirn								
39	Establish Community Team base office	1 day?	Mon 06/11/06	Mon 06/11/06										
40	Room availability	1 day?	Mon 06/11/06	Mon 06/11/06		Chris Rees;Jane Holdi								
41	Review all existing contratcs	0 days	Tue 07/11/06	Tue 07/11/06		Bob Feirn								
42	Risks	0 days	Tue 07/11/06	Tue 07/11/06		Team Managers								
43	Financial	0 days	Tue 07/11/06	Tue 07/11/06		Team Managers								
44	phase two	1 day	Mon 04/12/06	Mon 04/12/06		Bob Feirn								
45	evaluate change of service	0 days	Mon 04/12/06	Mon 04/12/06		Bob Feirn;Sue Coomb								
46	future developments	0 days	Mon 04/12/06	Mon 04/12/06		Team Managers								
47	management services	0 days	Mon 04/12/06	Mon 04/12/06		Team Managers								
48	support staffing	0 days	Mon 04/12/06	Mon 04/12/06		Team Managers								
49	phase three	0 days	Mon 18/12/06	Mon 18/12/06		Bob Feirn								
50	Audit service	0 days	Mon 18/12/06	Mon 18/12/06		Team Managers;Bob f								
51	Assess Service Quality	0 days	Mon 18/12/06	Mon 18/12/06		Team Managers;Bob f								


Project: Community Changes 04.10.06
Date: Wed 11/10/06

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

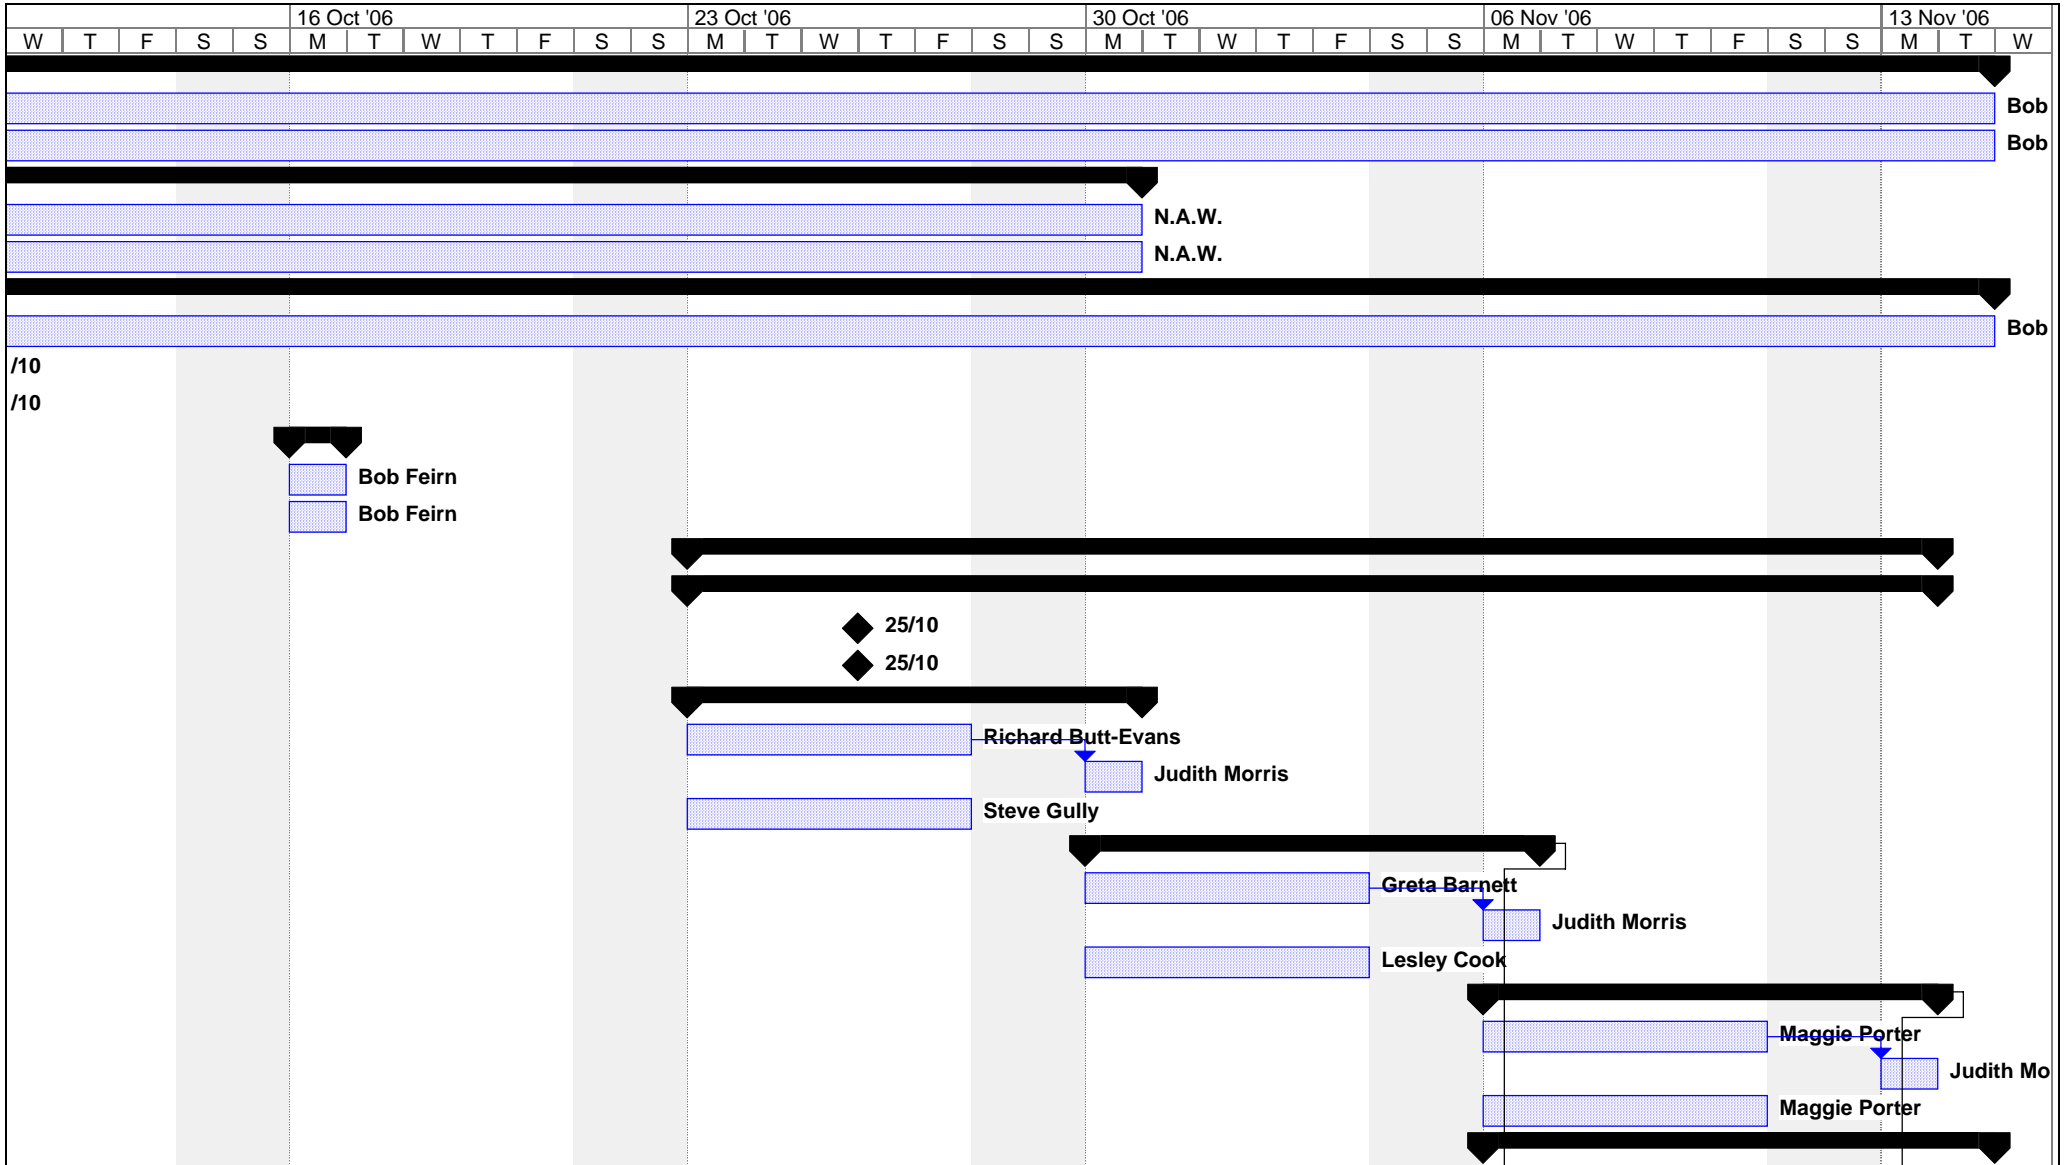





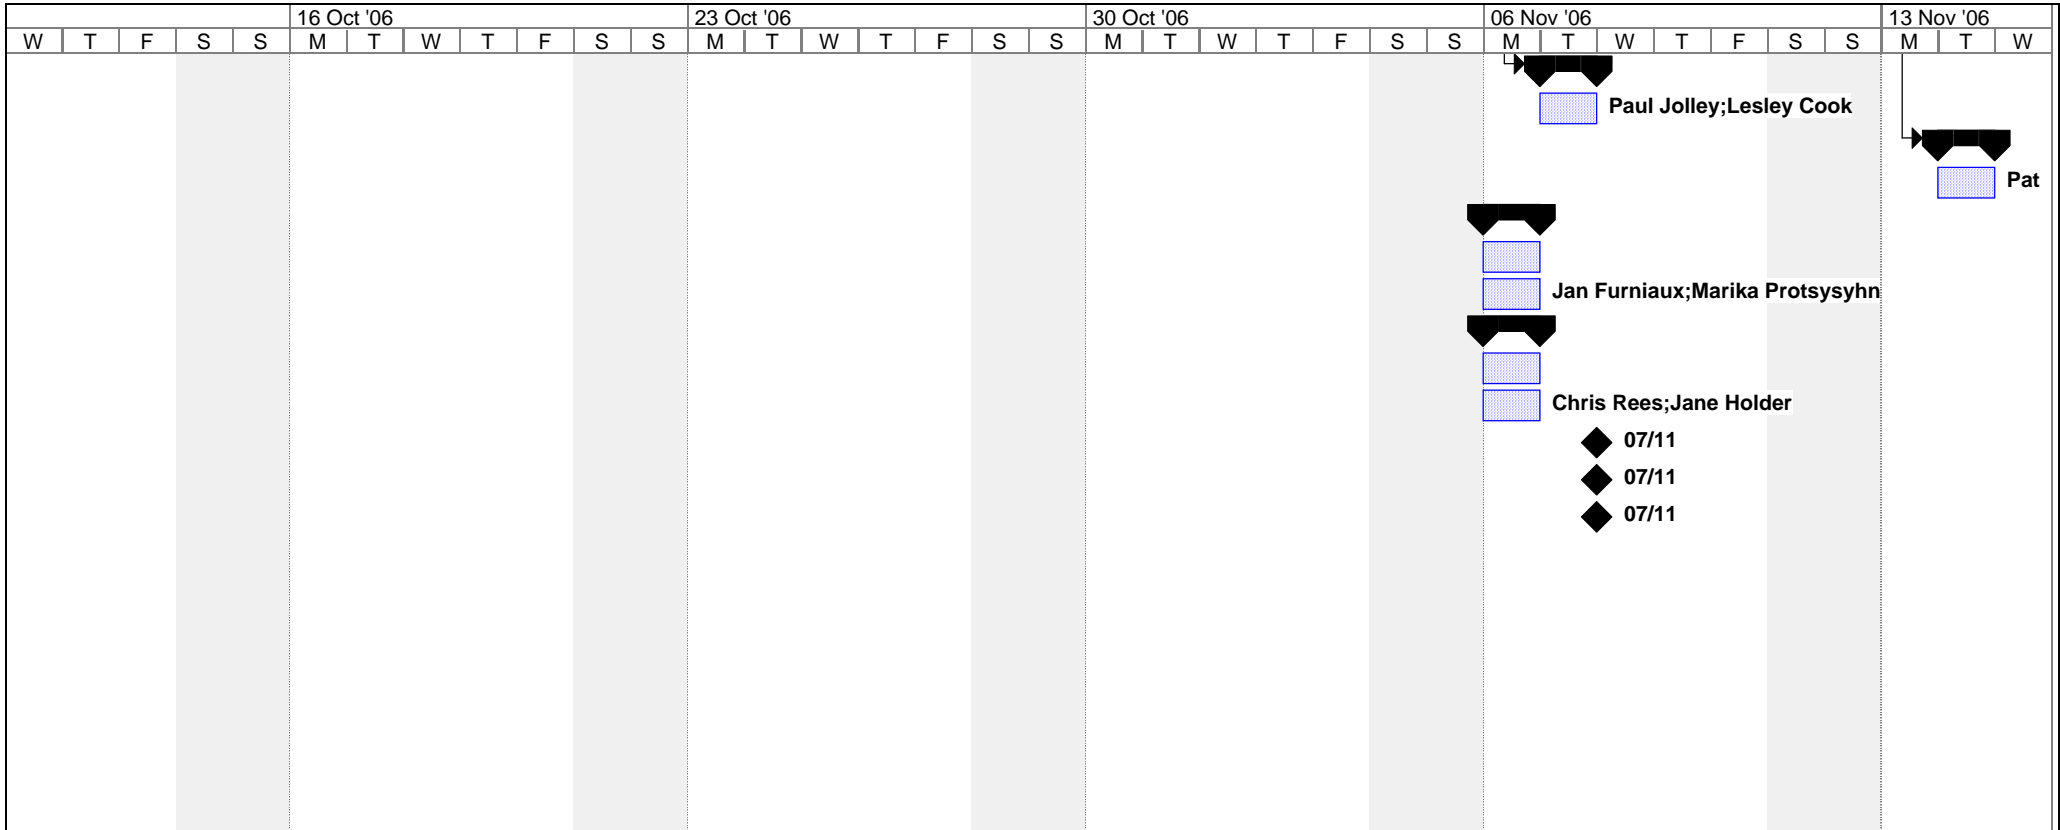




Project: Community Changes 04.10.06
 Date: Wed 11/10/06


Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	





Project: Community Changes 04.10.06 Date: Wed 11/10/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

				20 Nov '06				27 Nov '06				04 Dec '06				11 Dec '06				18 Dec '06								
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T
Feirn																												
Feirn																												
Feirn; Mike Race; Team Managers																												
rris																												

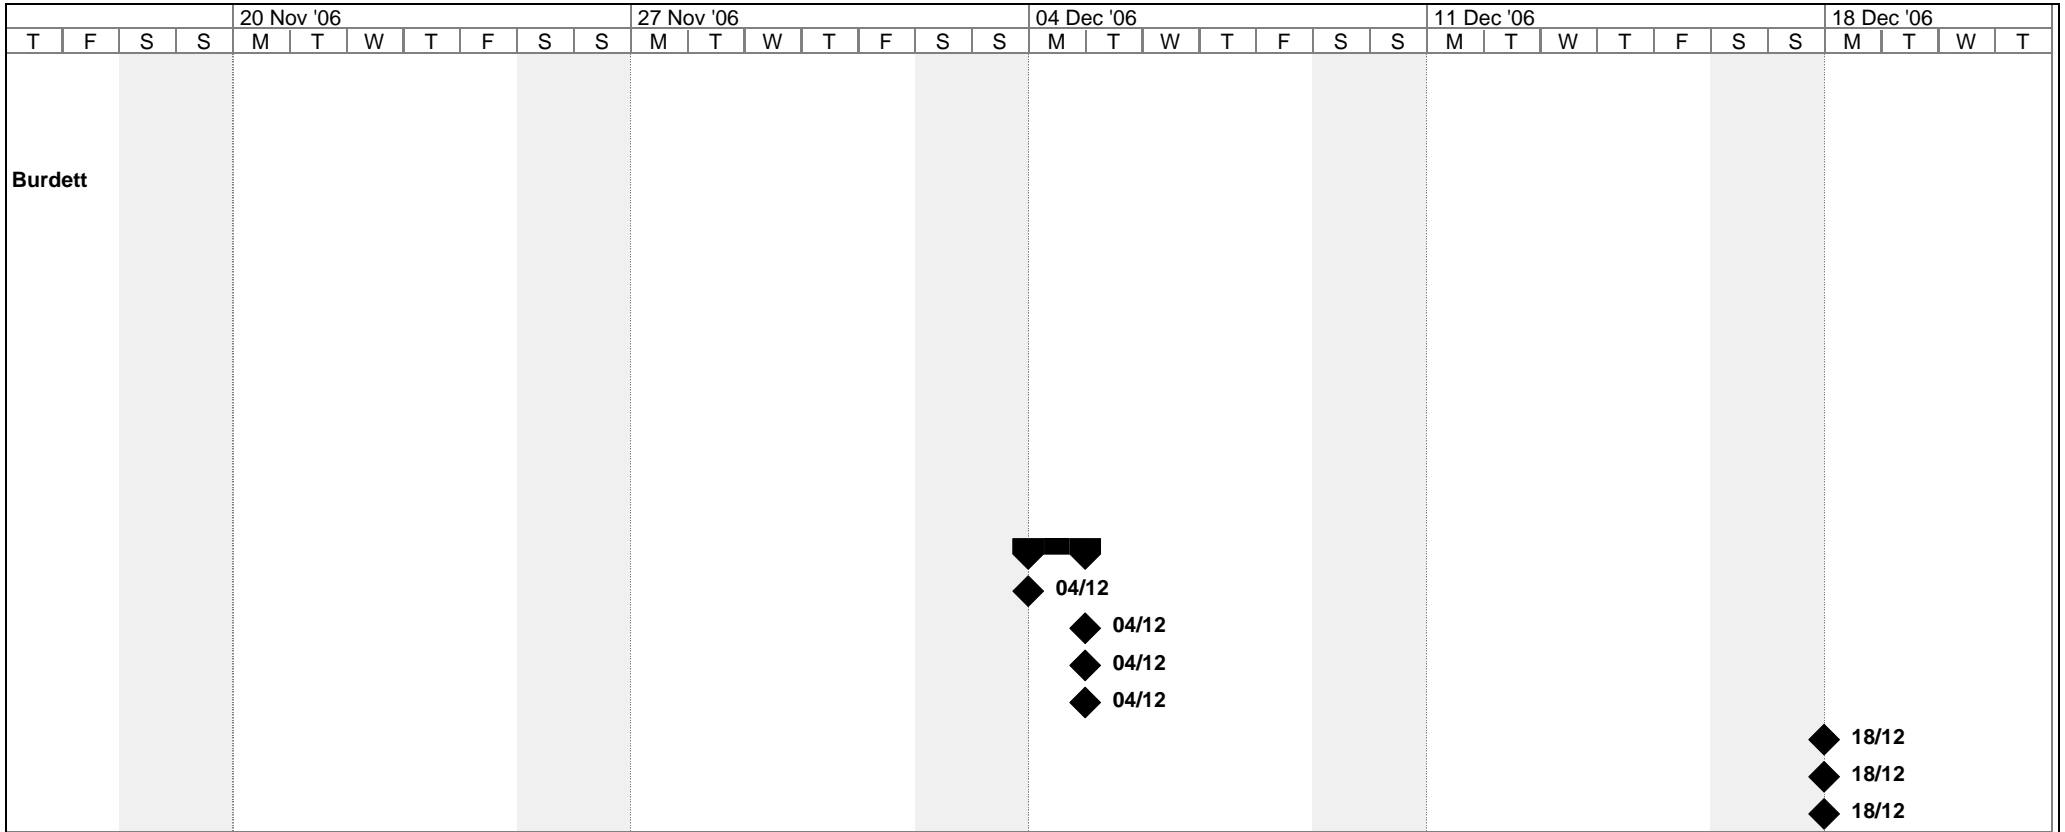Project: Community Changes 04.10.06 Date: Wed 11/10/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Community Changes 04.10.06 Date: Wed 11/10/06	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
